

ID		Task Mode	Task Name	Duration	Work	Start	Finish	Predecessors
0			Website Bán Sách Fahasa.com	85 days	1,997.41 hrs	Mon 06/10/25	Fri 30/01/26	
1			1.0 Thu thập & phân tích yêu cầu	38.92 days	388 hrs	Mon 06/10/25	Thu 27/11/25	
2			1.1 Xây dựng bảng khảo sát người dùng	4 days	32 hrs	Mon 06/10/25	Thu 09/10/25	
3			1.2 Thu thập yêu cầu người dùng	11.5 days	92 hrs	Fri 10/10/25	Mon 27/10/25	2
4			1.3 Phân tích kết quả khảo sát	9 days	72 hrs	Wed 15/10/25	Tue 28/10/25	3FS-8 days
5			1.4 Phân tích yêu cầu chức năng	10 days	80 hrs	Mon 27/10/25	Mon 10/11/25	4SS+8 days
6			1.5 Xác định luồng tương tác	5 days	40 hrs	Mon 10/11/25	Mon 17/11/25	5SS+9 days
7			1.6 Xác định các Stakeholder	4 days	32 hrs	Tue 18/11/25	Tue 25/11/25	6SS-7 days
8			1.7 Viết tài liệu yêu cầu phần mềm (SRS)	5 days	40 hrs	Thu 20/11/25	Thu 27/11/25	7SS+2 days
9			Hoàn thành phân tích	0 days	0 hrs	Thu 27/11/25	Thu 27/11/25	8
10			2.0 Thiết kế hệ thống	20.5 days	152.8 hrs	Fri 17/10/25	Fri 14/11/25	
11			2.1 Thiết kế giao diện người dùng (UI/UX)	9 days	80.8 hrs	Fri 17/10/25	Thu 30/10/25	4FS-7 days
12			2.2 Thiết kế kiến trúc web	2 days	16 hrs	Thu 30/10/25	Mon 03/11/25	5FS-7 days
13			2.3 Thiết kế và kết nối cơ sở dữ liệu	2 days	16 hrs	Mon 03/11/25	Wed 05/11/25	12SS+1 day
14			2.4 Thiết kế API và tích hợp	2 days	16 hrs	Mon 10/11/25	Tue 11/11/25	13SS+1 day

Project: Website Bán Sách Fahasa.com Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

ID		Task Mode	Task Name	Duration	Work	Start	Finish	Predecessors
15			2.5 Viết tài liệu thiết kế phần mềm (SWD)	3 days	24 hrs	Wed 12/11/25	Fri 14/11/25	14SS-2 days
16			Hoàn thành thiết kế	0 days	0 hrs	Fri 14/11/25	Fri 14/11/25	15
17			3.0 Phát triển phần mềm	50 days	581.2 hrs	Mon 27/10/25	Fri 02/01/26	
18			3.1 Frontend	33 days	252 hrs	Mon 27/10/25	Wed 10/12/25	
19			3.1.1 Xây dựng trang ch	3 days	24 hrs	Mon 27/10/25	Wed 29/10/25	11SS+2 days
20			3.1.2 Xây dựng trang sản phẩm	2 days	16 hrs	Mon 03/11/25	Tue 04/11/25	19SS+1 day
21			3.1.3 Xây dựng trang chi tiết sản phẩm	2 days	16 hrs	Wed 05/11/25	Thu 06/11/25	20SS+1 day
22			3.1.4 Xây dựng trang sách giáo khoa	2 days	16 hrs	Fri 07/11/25	Mon 10/11/25	21SS+2 days
23			3.1.5 Xây dựng giỏ hàng	2 days	16 hrs	Tue 11/11/25	Wed 12/11/25	22SS+2 days
24			3.1.6 Xây dựng trang Flash Sale	2 days	16 hrs	Mon 17/11/25	Tue 18/11/25	23SS+2 days
25			3.1.7 Xây dựng trang mã khuyến mãi	2 days	16 hrs	Wed 19/11/25	Thu 20/11/25	24SS+2 days
26			3.1.8 Xây dựng trang sản phẩm mới	2 days	16 hrs	Fri 21/11/25	Mon 24/11/25	25SS+2 days
27			3.1.9 Xây dựng form đăng ký	0.5 days	4 hrs	Tue 25/11/25	Tue 25/11/25	26SS+2 days
28			3.1.10 Xây dựng form đăng nhập	0.5 days	4 hrs	Wed 03/12/25	Wed 03/12/25	27SS+1 day
29			3.1.11 Xây dựng form khôi phục mật khẩu	0.5 days	4 hrs	Tue 09/12/25	Tue 09/12/25	28SS+1 day

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

ID		Task Mode	Task Name	Duration	Work	Start	Finish	Predecessors
30			3.1.12 Xây dựng trang thông tin tài khoản	1 day	8 hrs	Mon 17/11/25	Mon 17/11/25	16SS-1 day
31			3.1.13 Xây dựng trang sổ địa chỉ	2 days	16 hrs	Tue 18/11/25	Wed 19/11/25	30SS
32			3.1.14 Xây dựng trang đổi mật khẩu	1 day	8 hrs	Thu 20/11/25	Thu 20/11/25	31SS+1 day
33			3.1.15 Xây dựng trang đơn hàng	2 days	16 hrs	Fri 21/11/25	Mon 24/11/25	32SS+1 day
34			3.1.16 Xây dựng trang chi tiết đơn hàng	2 days	16 hrs	Tue 25/11/25	Wed 26/11/25	33SS+1 day
35			3.1.17 Xây dựng trang thông báo	1 day	8 hrs	Thu 27/11/25	Thu 27/11/25	34SS+1 day
36			3.1.18 Xây dựng trang ưu đãi thành viên	2 days	16 hrs	Mon 01/12/25	Wed 03/12/25	35SS+1 day
37			3.1.19 Xây dựng trang ví voucher	1 day	8 hrs	Thu 04/12/25	Thu 04/12/25	36SS+1 day
38			3.1.20 Xây dựng trang tài khoản	1 day	8 hrs	Wed 10/12/25	Wed 10/12/25	37SS+1 day
39			3.2 Backend	47 days	329.2 hrs	Thu 30/10/25	Fri 02/01/26	
40			3.2.1 Xác thực & phân quyền người dùng	1 day	8 hrs	Tue 09/12/25	Tue 09/12/25	15SS+2 days
41			3.2.2 Lập trình Trang ch	2 days	16 hrs	Thu 30/10/25	Fri 31/10/25	19SS+2 days
42			3.2.3 Lập trình Trang sản phẩm	2 days	16 hrs	Tue 25/11/25	Fri 28/11/25	20SS+2 days
43			3.2.4 Lập trình Trang chi tiết sản phẩm	1 day	8 hrs	Tue 02/12/25	Wed 03/12/25	21SS+2 days

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

ID		Task Mode	Task Name	Duration	Work	Start	Finish	Predecessors
44			3.2.5 Lập trình Trang sách giáo khoa	2 days	16 hrs	Thu 13/11/25	Tue 02/12/25	22SS+2 days
45			3.2.6 Lập trình Giỏ hàng	1 day	8 hrs	Fri 14/11/25	Tue 02/12/25	23SS+2 days
46			3.2.7 Lập trình Trang Flash Sale	2 days	16 hrs	Thu 04/12/25	Fri 05/12/25	24SS+2 days
47			3.2.8 Lập trình Trang mã khuyến mãi	1 day	8 hrs	Wed 26/11/25	Mon 01/12/25	25SS+2 days
48			3.2.9 Lập trình Trang sản phẩm mới	2 days	16 hrs	Thu 27/11/25	Fri 19/12/25	26SS+2 days
49			3.2.10 Lập trình Đăng ký	0.5 days	4 hrs	Fri 28/11/25	Fri 28/11/25	27SS+2 days
50			3.2.11 Lập trình Đăng nhập	0.5 days	4 hrs	Mon 08/12/25	Mon 08/12/25	28SS+2 days
51			3.2.12 Lập trình Khôi phục mật khẩu	0.5 days	4 hrs	Mon 22/12/25	Mon 22/12/25	29SS+2 days
52			3.2.13 Lập trình Trang thông tin tài khoản	1 day	8 hrs	Mon 08/12/25	Mon 08/12/25	30SS+2 days
53			3.2.14 Lập trình Trang sổ địa chỉ	1 day	8 hrs	Fri 05/12/25	Fri 05/12/25	31SS+2 days
54			3.2.15 Lập trình Trang đổi mật khẩu	0.5 days	4 hrs	Mon 22/12/25	Mon 22/12/25	32SS+2 days
55			3.2.16 Lập trình Trang đơn hàng	1 day	8 hrs	Fri 12/12/25	Wed 17/12/25	33SS+2 days
56			3.2.17 Lập trình Trang chi tiết đơn hàng	1 day	8 hrs	Fri 28/11/25	Fri 28/11/25	34SS+2 days
57			3.2.18 Lập trình Trang thông báo	1 day	8 hrs	Tue 02/12/25	Tue 02/12/25	35SS+2 days

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	


ID		Task Mode	Task Name	Duration	Work	Start	Finish	Predecessors
58			3.2.19 Lập trình Trang ưu đãi thành viên	1 day	8 hrs	Mon 15/12/25	Mon 15/12/25	36SS+2 days
59			3.2.20 Lập trình Trang ví voucher	1 day	8 hrs	Thu 11/12/25	Thu 11/12/25	37SS+2 days
60			3.2.21 Lập trình Trang tài khoản	1 day	8 hrs	Tue 16/12/25	Tue 16/12/25	38SS+2 days
61			3.2.22 Xử lý thanh toán & giao dịch	2 days	16 hrs	Wed 17/12/25	Tue 23/12/25	60SS
62			3.2.23 Bảo mật hệ thố	6.5 days	52 hrs	Mon 08/12/25	Wed 17/12/25	50SS-2 days
63			3.2.24 Gửi email & thông báo hệ thống	1 day	8 hrs	Tue 23/12/25	Wed 24/12/25	61SS+3 days
64			3.2.25 Tối ưu hiệu năng Backend	6.5 days	61.2 hrs	Thu 25/12/25	Fri 02/01/26	60SS
65			Hoàn thành lập trình	0 days	0 hrs	Fri 02/01/26	Fri 02/01/26	64
66			4.0 Tích hợp hệ thống	29.5 days	36 hrs	Thu 18/12/25	Wed 28/01/26	
67			4.1 Tích hợp cổng thanh toán (VNPAY, MoMo...)	2.5 days	12 hrs	Thu 18/12/25	Mon 22/12/25	
68			4.1.1 Đăng ký tài khoản đối tác VNPAY &	0.5 days	4 hrs	Thu 18/12/25	Thu 18/12/25	62
69			4.1.2 Tích hợp API thanh toán (VNPAY,	1 day	8 hrs	Thu 18/12/25	Mon 22/12/25	68SS
70			4.2 Tích hợp bản đồ & tra cứu vận chuyển	1.5 days	12 hrs	Tue 23/12/25	Thu 25/12/25	
71			4.2.1 Tích hợp API Google Maps (địa chỉ,	0.5 days	4 hrs	Tue 23/12/25	Wed 24/12/25	69

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

ID		Task Mode	Task Name	Duration	Work	Start	Finish	Predecessors
72			4.2.2 Tích hợp API tra cứu vận đơn (GHN,	1 day	8 hrs	Wed 24/12/25	Thu 25/12/25	71SS
73			4.3 Tích hợp đăng nhập mạng xã hội (Facebook,	1.5 days	12 hrs	Mon 29/12/25	Wed 28/01/26	72SS
74			Hoàn thành tích hợp	0 days	0 hrs	Wed 28/01/26	Wed 28/01/26	73
75			5.0 Kiểm thử và triển khai website	68.5 days	839.41 hrs	Tue 28/10/25	Fri 30/01/26	
76			5.1 Viết test case	16 days	128 hrs	Tue 28/10/25	Mon 15/12/25	5SS+1 day
77			5.2 Triển khai hệ thống lên môi trường test	1.5 days	12 hrs	Thu 18/12/25	Fri 19/12/25	38SS+6 days
78			5.3 Kiểm thử giao diện	12 days	96 hrs	Tue 09/12/25	Thu 25/12/25	22SS-12 days
79			5.4 Kiểm thử chức năng	14 days	112 hrs	Fri 31/10/25	Wed 19/11/25	41FS-1 day
80			5.5 Kiểm thử bảo mật & hiệu năng	10 days	80 hrs	Fri 19/12/25	Fri 09/01/26	79FS-2 days
81			5.6 Kiểm thử thanh toán ở môi trường sandbox	2.5 days	20 hrs	Mon 12/01/26	Wed 14/01/26	80FS-3 days
82			5.7 Kiểm thử tra cứu vận chuyển theo mã đơn	2.5 days	20 hrs	Tue 13/01/26	Thu 15/01/26	81FS-2 days
83			5.8 Kiểm thử tích hợp	11 days	88 hrs	Mon 17/11/25	Tue 09/12/25	79FS-3 days
84			5.9 Kiểm thử chấp nhận người dùng	3 days	24 hrs	Thu 08/01/26	Wed 14/01/26	80FS-1 day
85			5.10 Xử lý lỗi	15.5 days	155.41 hrs	Mon 05/01/26	Mon 26/01/26	83SS+1 day
86			5.11 Triển khai website	3 days	24 hrs	Mon 26/01/26	Fri 30/01/26	85FS-2 days
87			5.12 Viết tài liệu hướng dẫn cài đặt	5 days	40 hrs	Fri 09/01/26	Thu 15/01/26	85SS+3 days

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

ID		Task Mode	Task Name	Duration	Work	Start	Finish	Predecessors
88			5.13 Viết tài liệu Hướng dẫn sử dụng	5 days	40 hrs	Fri 02/01/26	Thu 08/01/26	83SS+6 days
89			Hoàn thành kiểm thử & triển khai website	0 days	0 hrs	Thu 08/01/26	Thu 08/01/26	88

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

[illegible]

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

Resource Names

Developer A

Developer A

Developer A

Developer A

Developer A

Developer A

Developer A

Developer A

Developer A

Developer A

Developer B

Developer B

Developer B

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

Project: Website Bán Sách Faha
Date: Sun 13/09/26


Page 10

[illegible]

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

Resource Names	05 Oct '25							12 Oct '25							19 Oct '25							26 Oct '25							02 Nov '25							09 N	
	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
Developer A																																					
Developer A																																					
Developer A																																					
Developer A																																					
Developer B																																					
Developer A																																					
Developer A[90%],Developer																																					
Developer B																																					
Developer B																																					
Developer B																																					

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

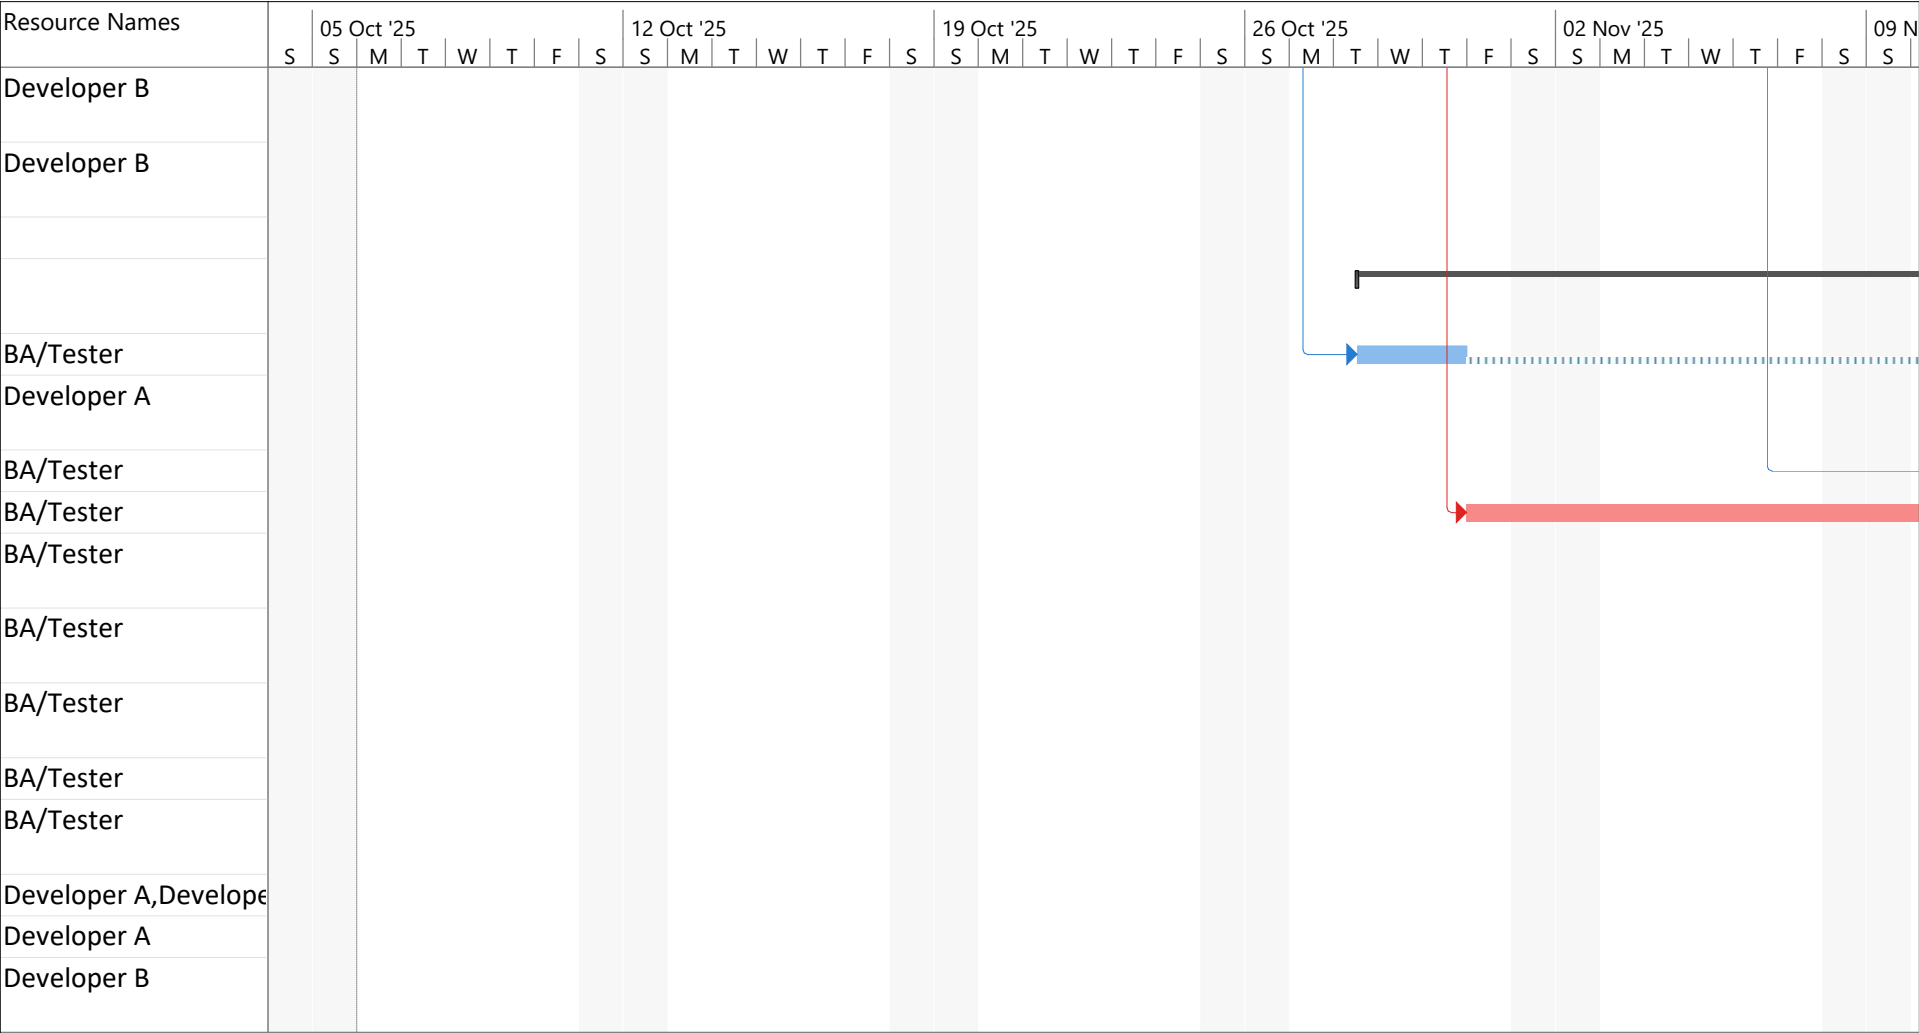

Project: Website Bán Sách Faha
Date: Sun 13/09/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone


Deadline

Critical


Critical Split


Progress


Manual Progress

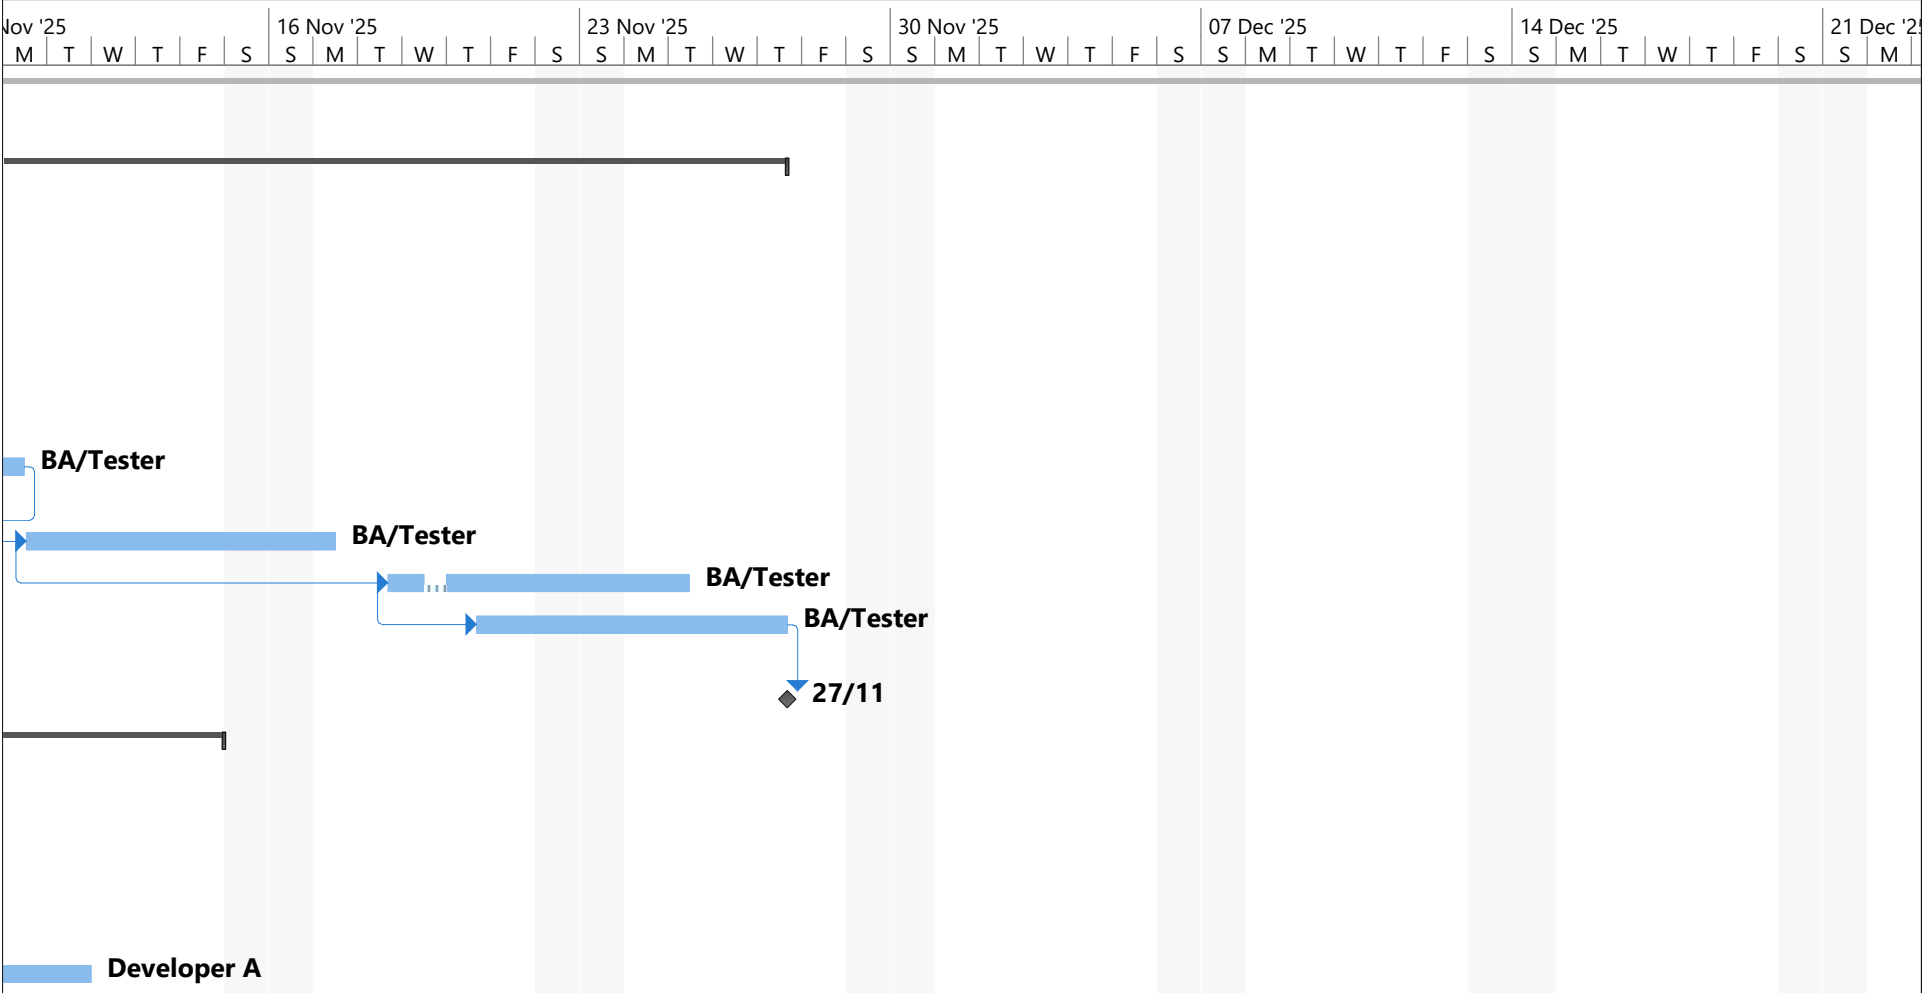


Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

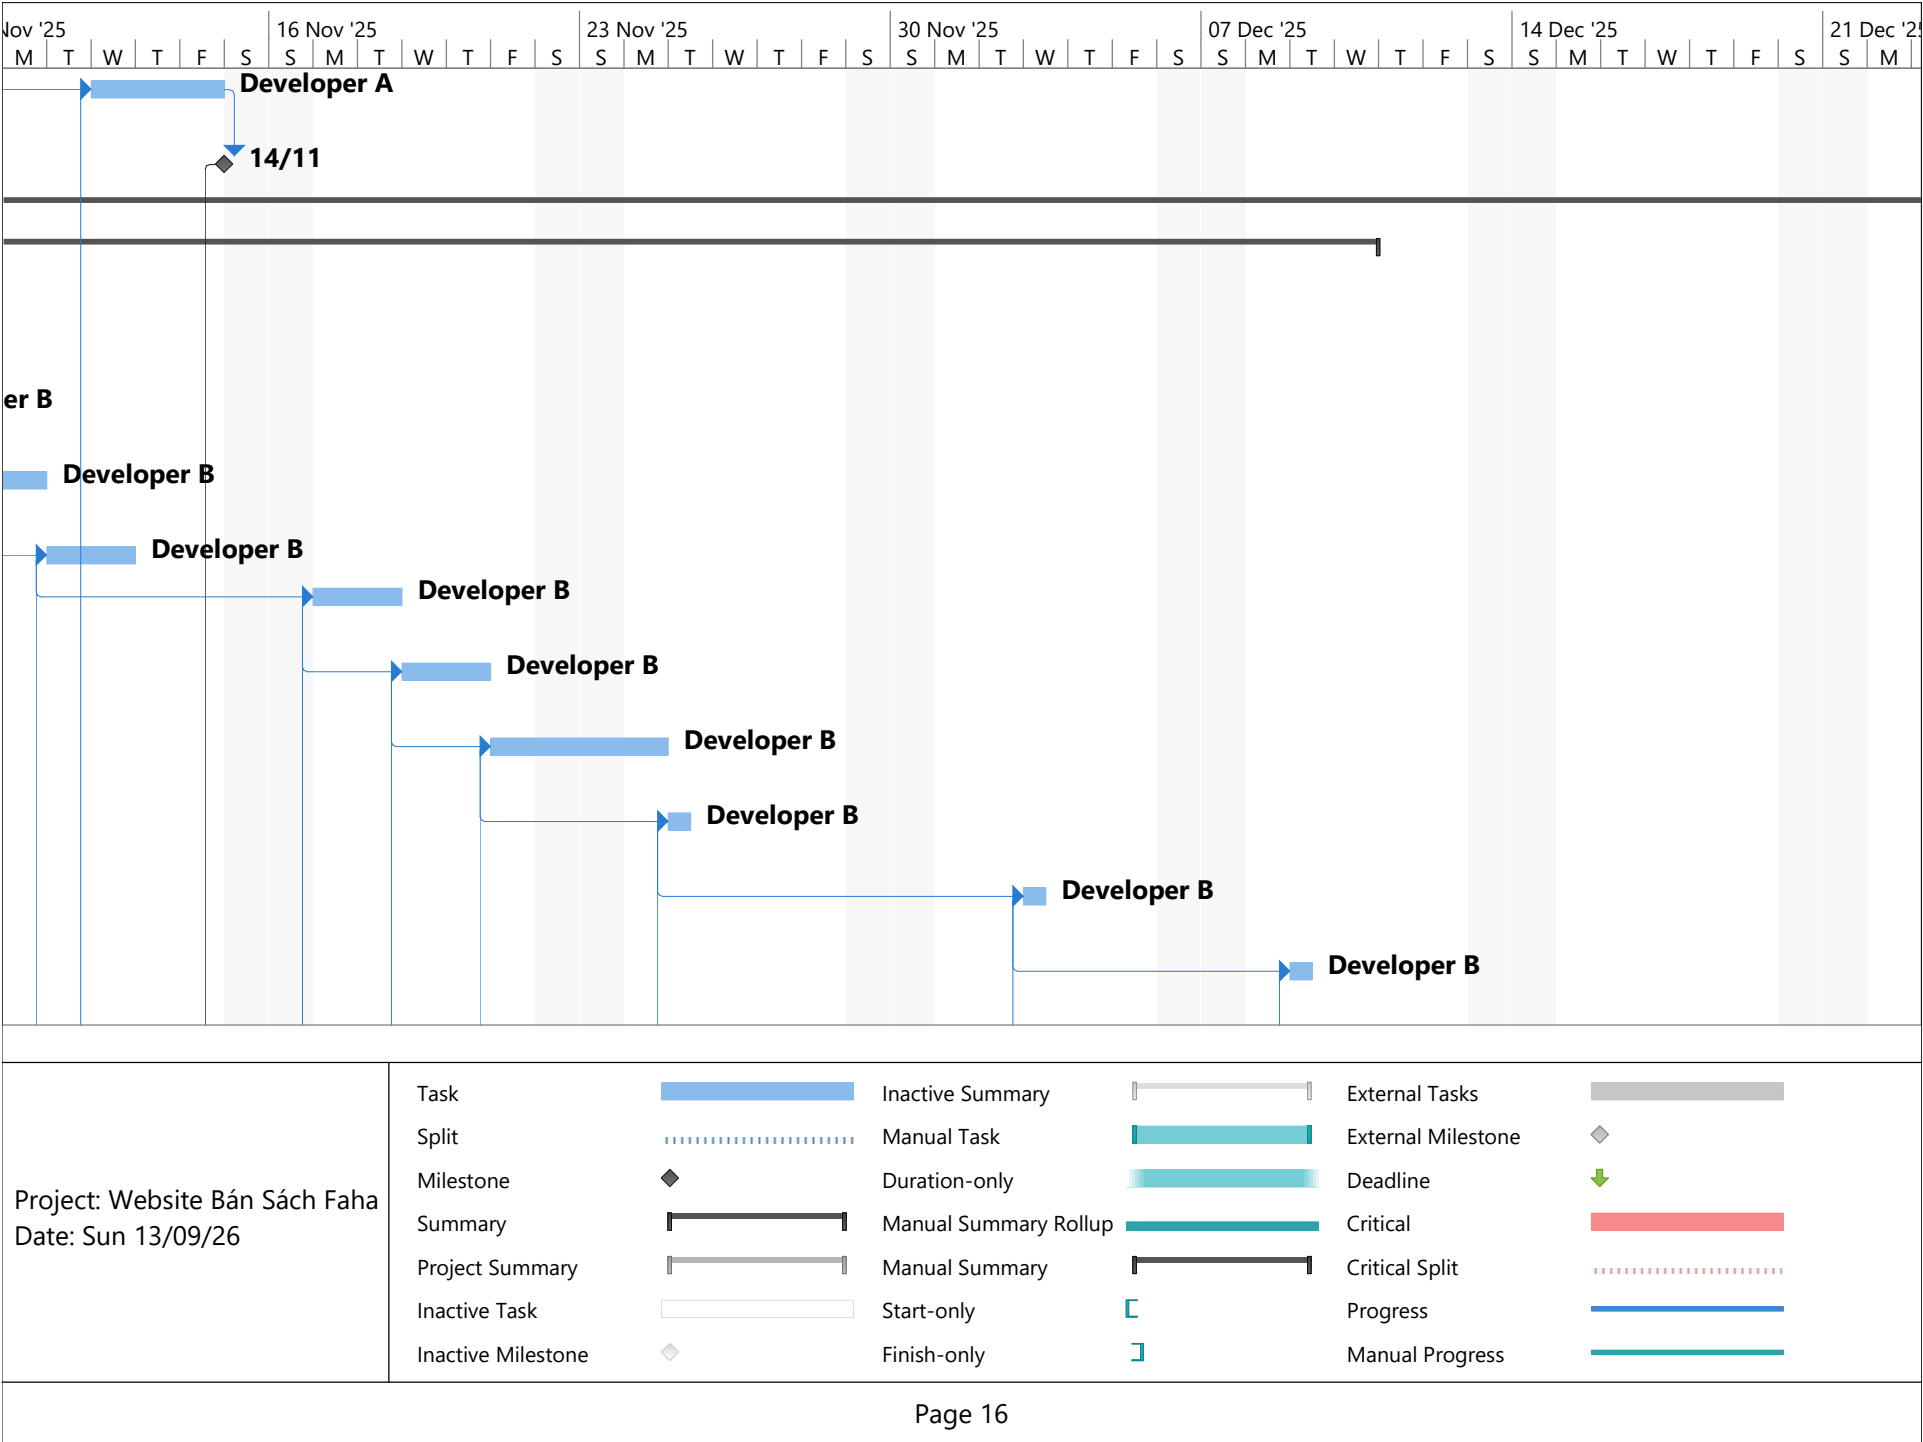

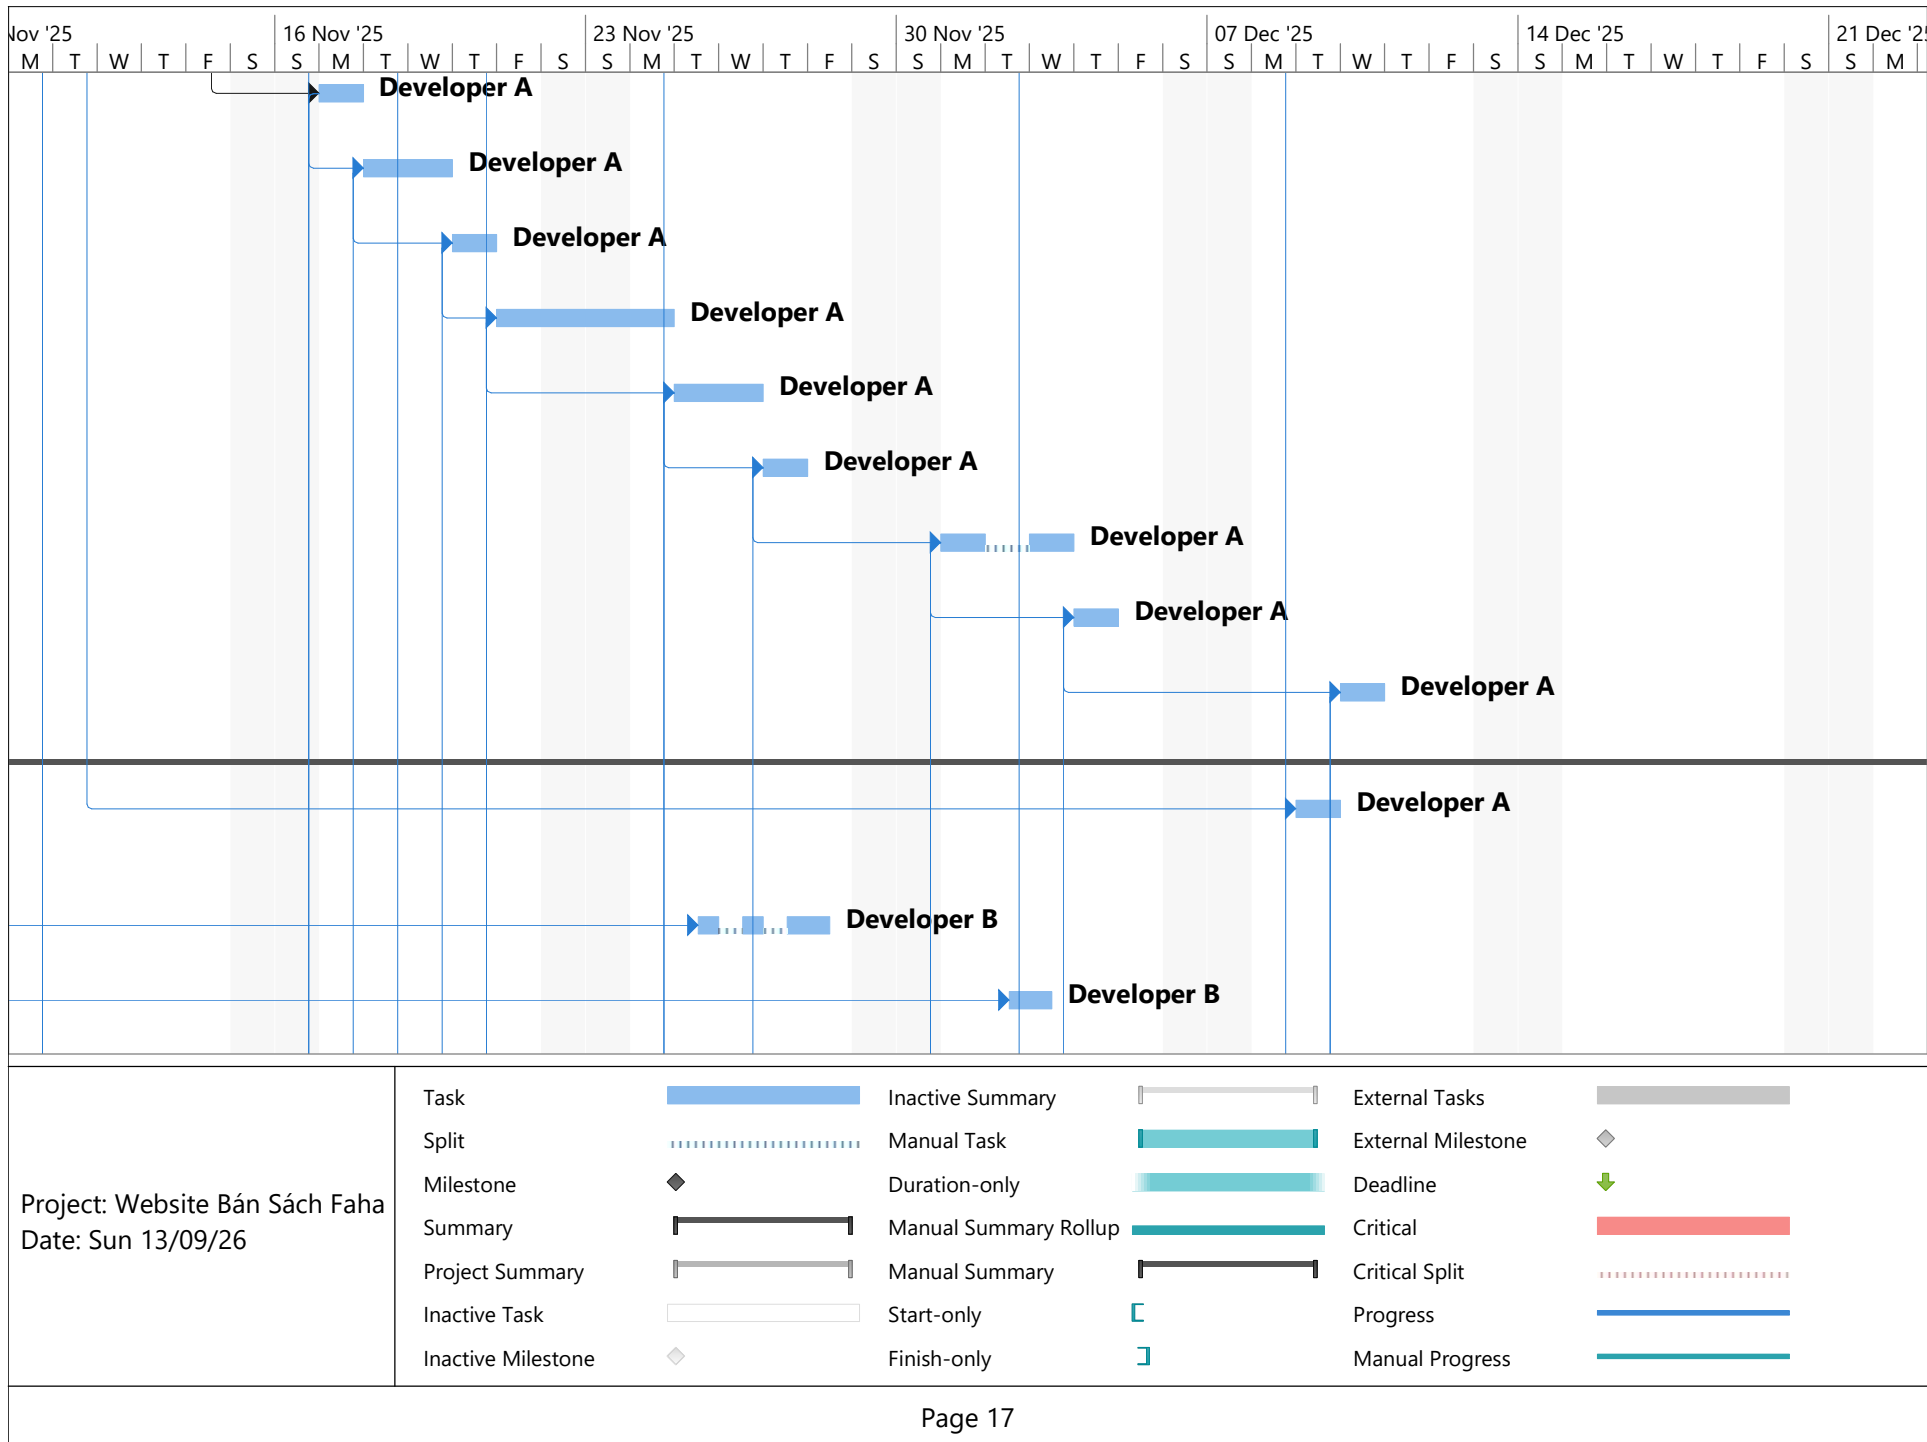


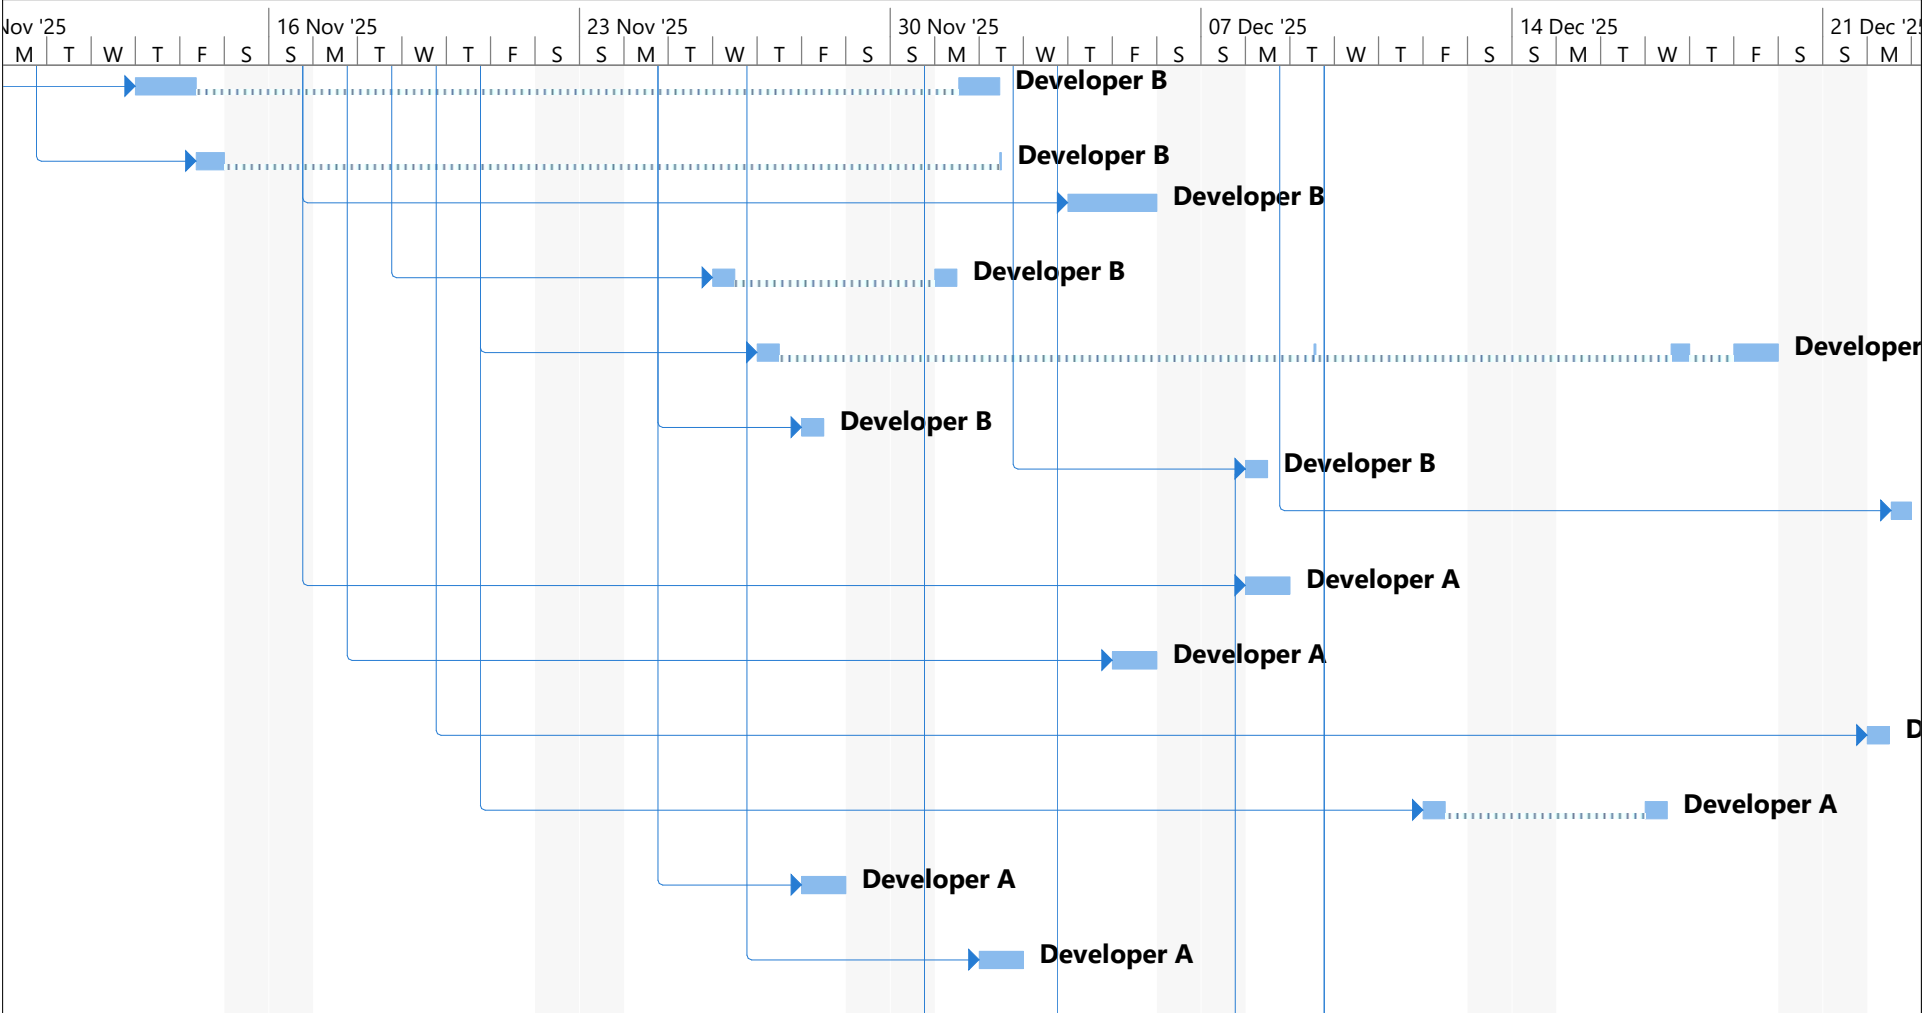


Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

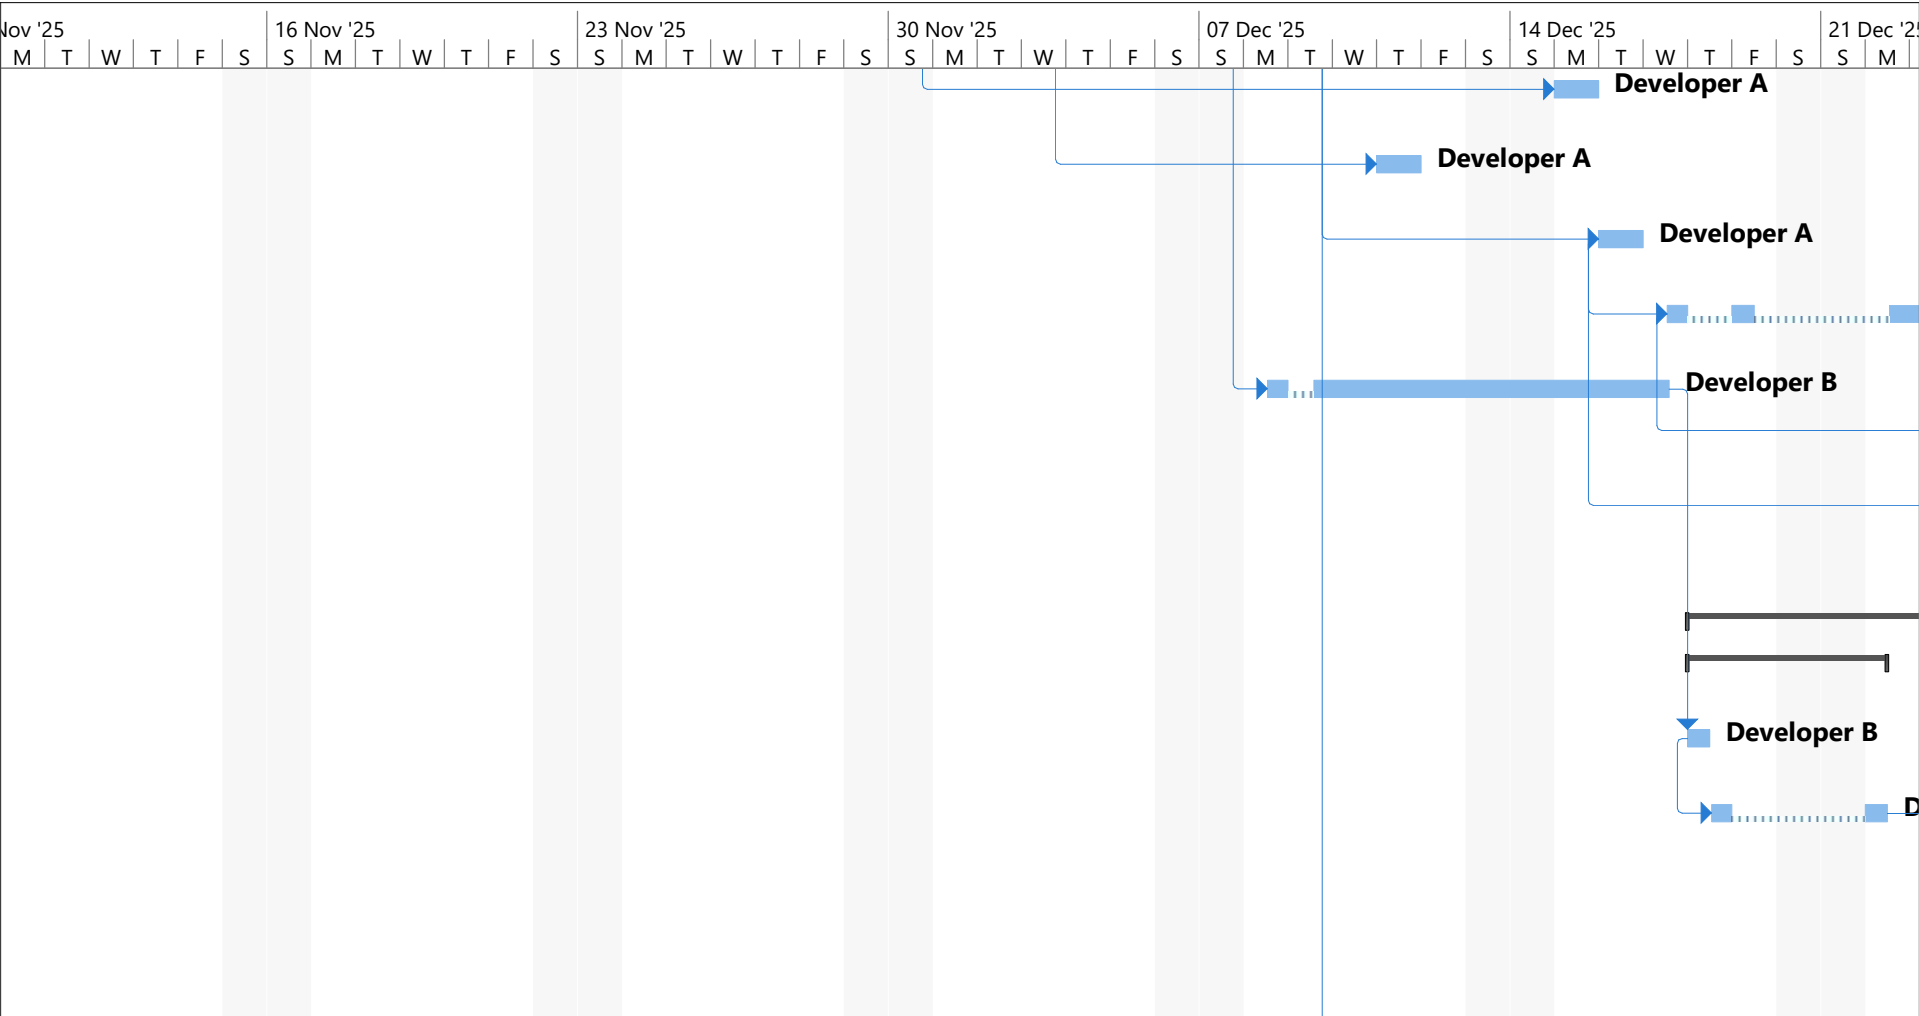


Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

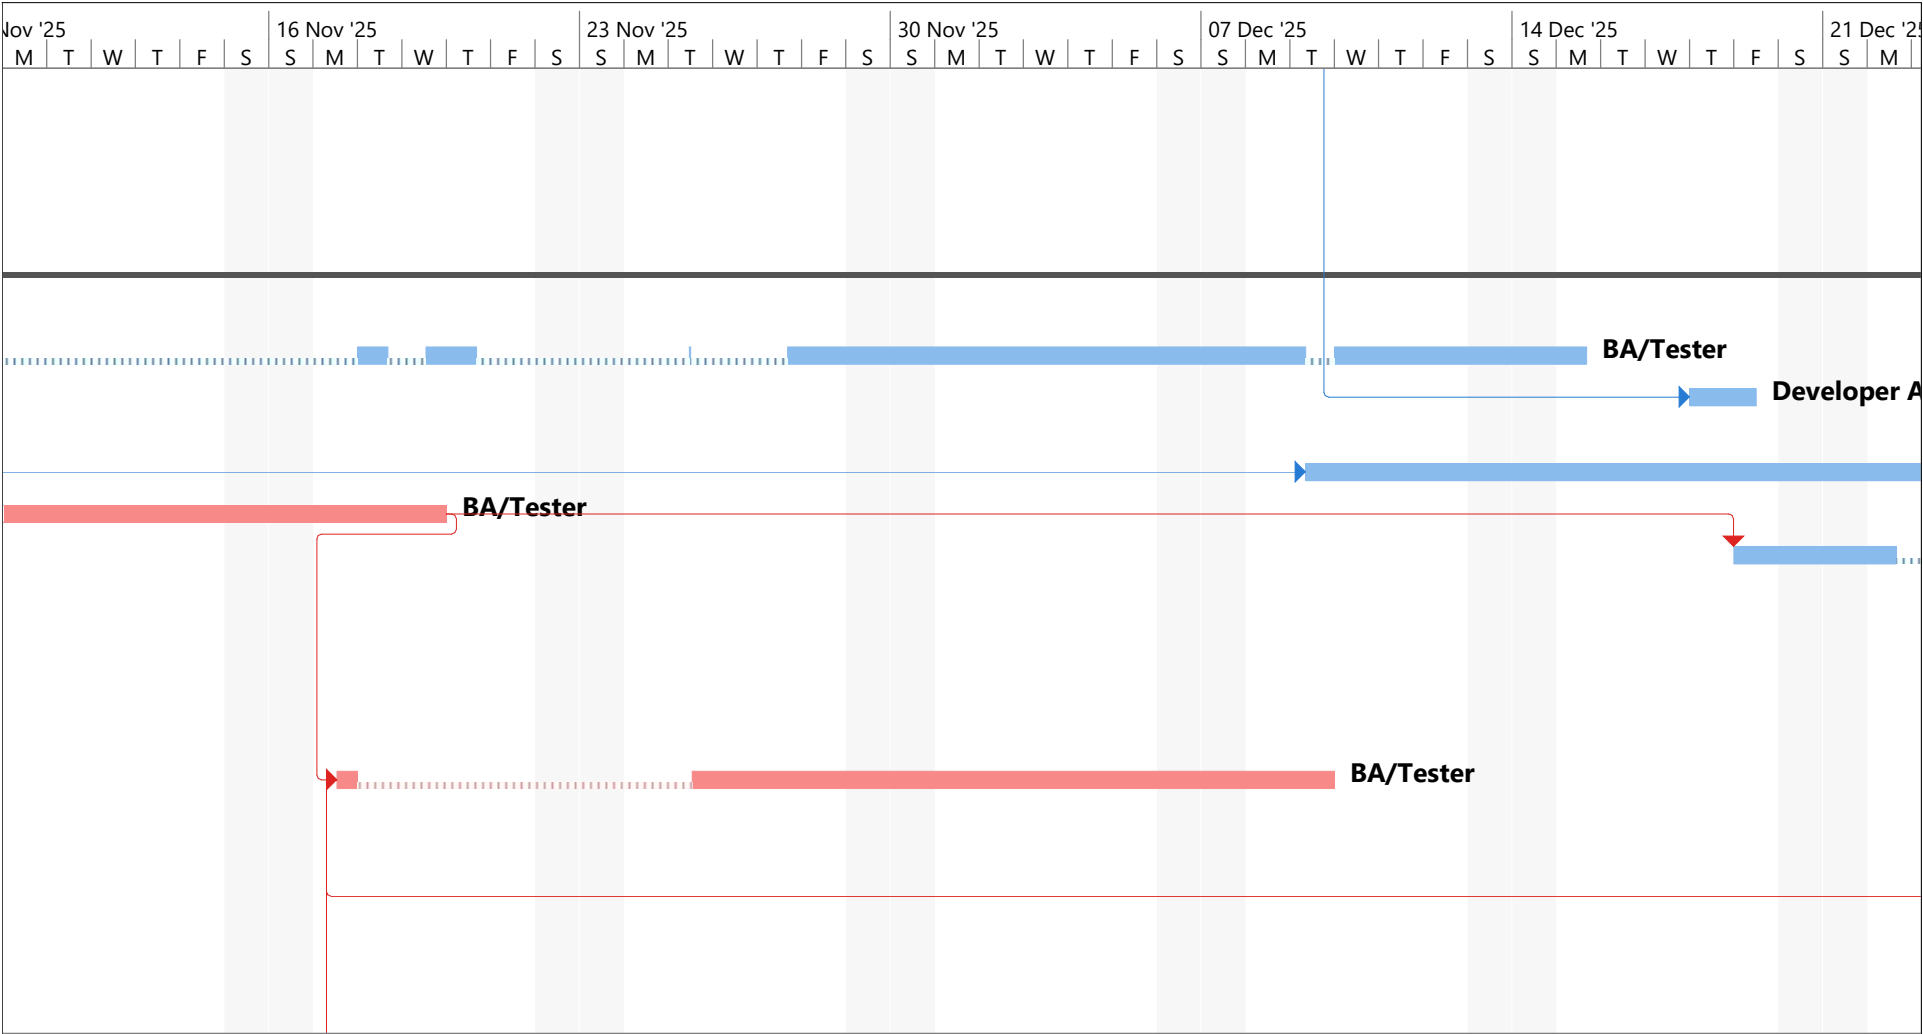

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

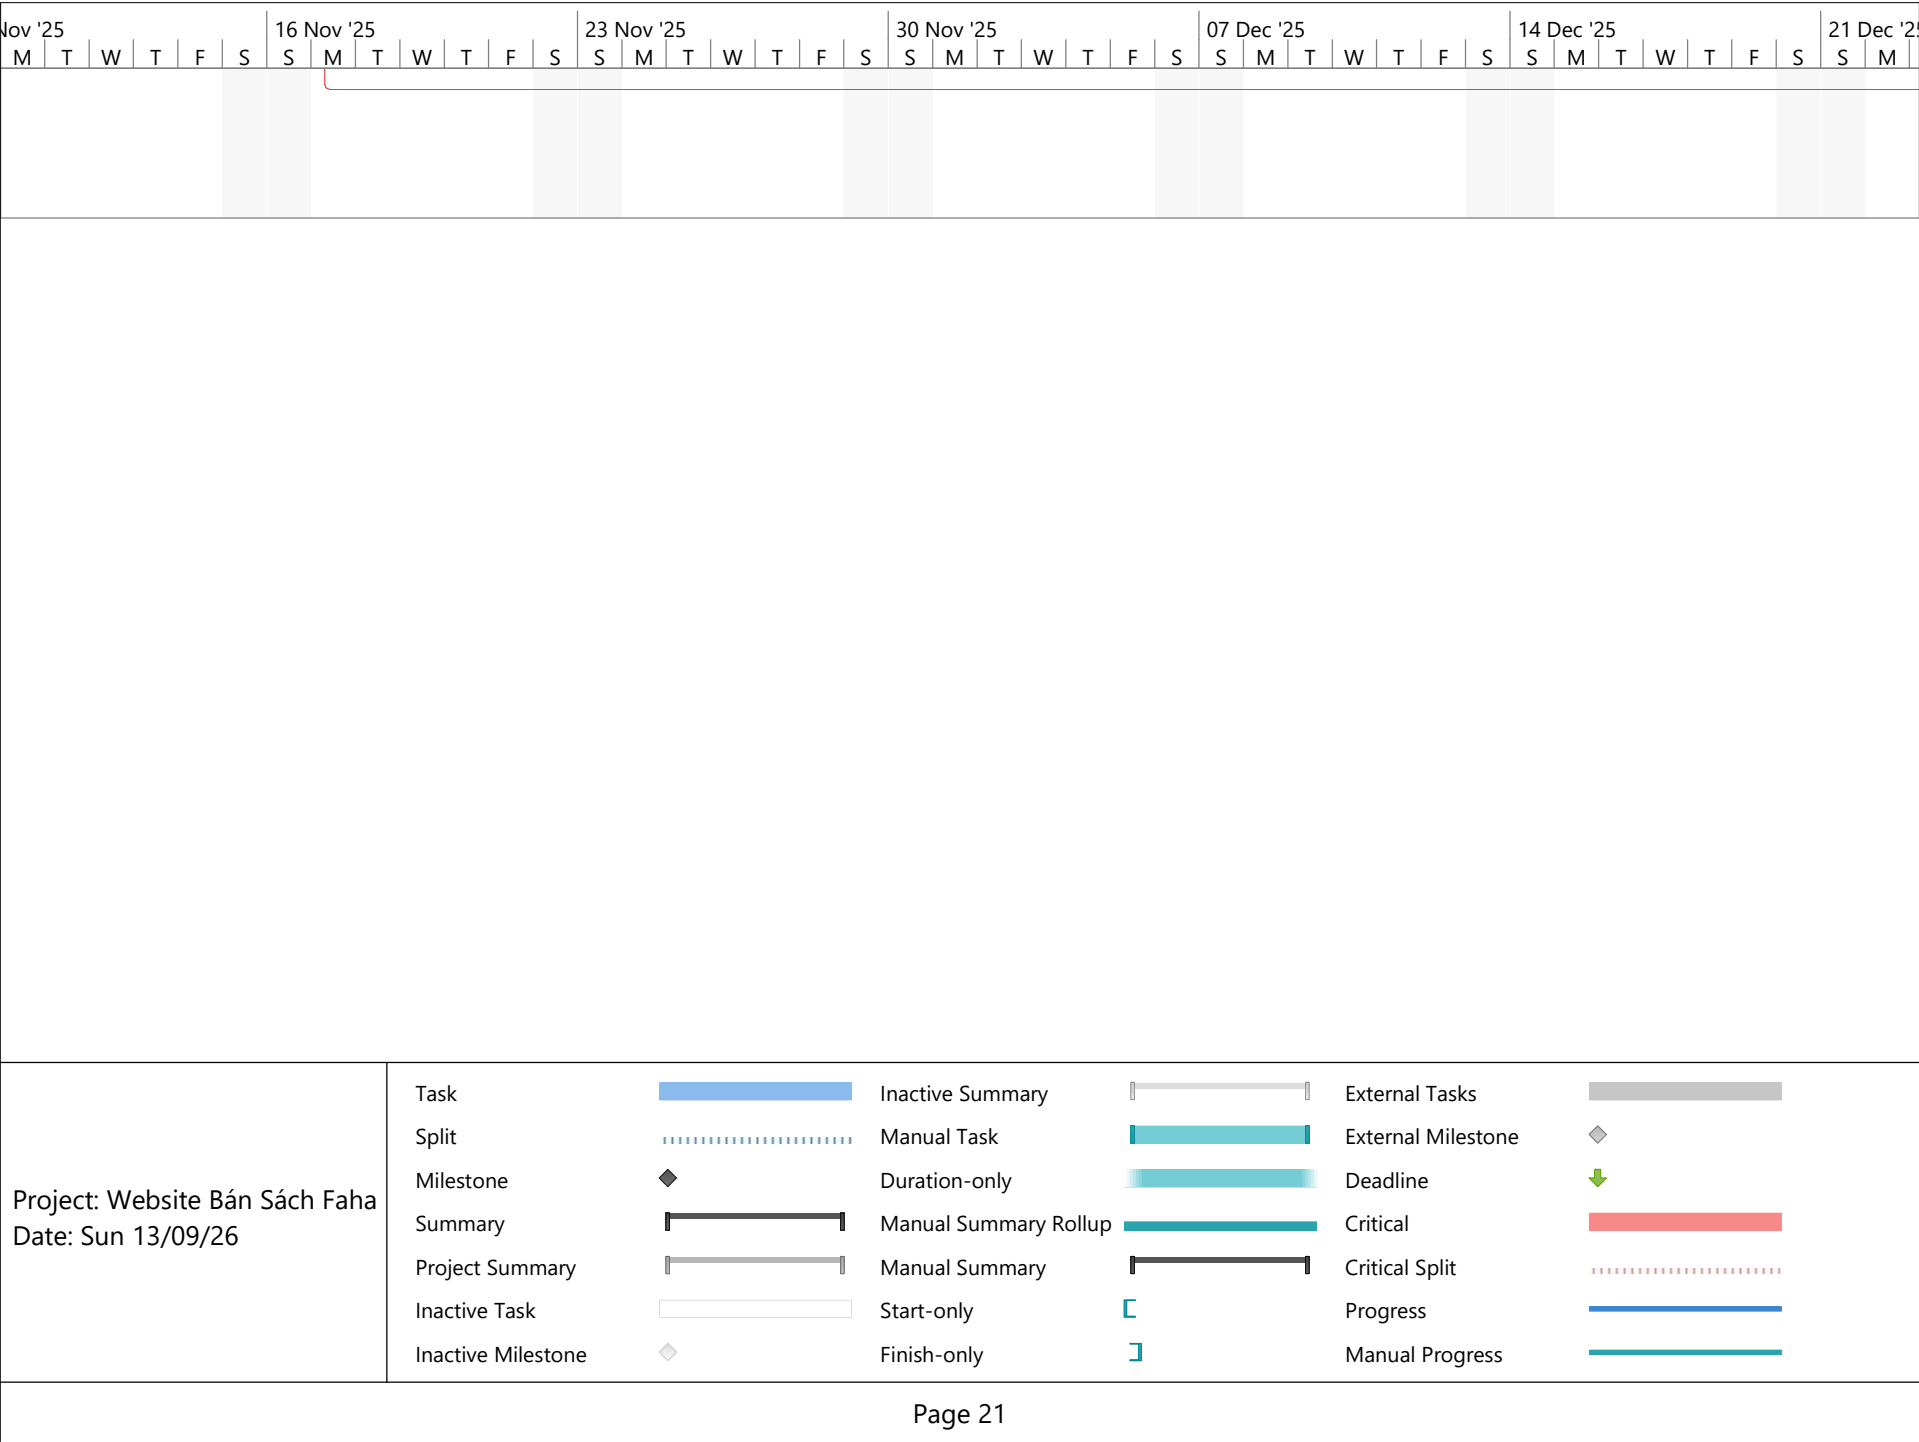

Page 21

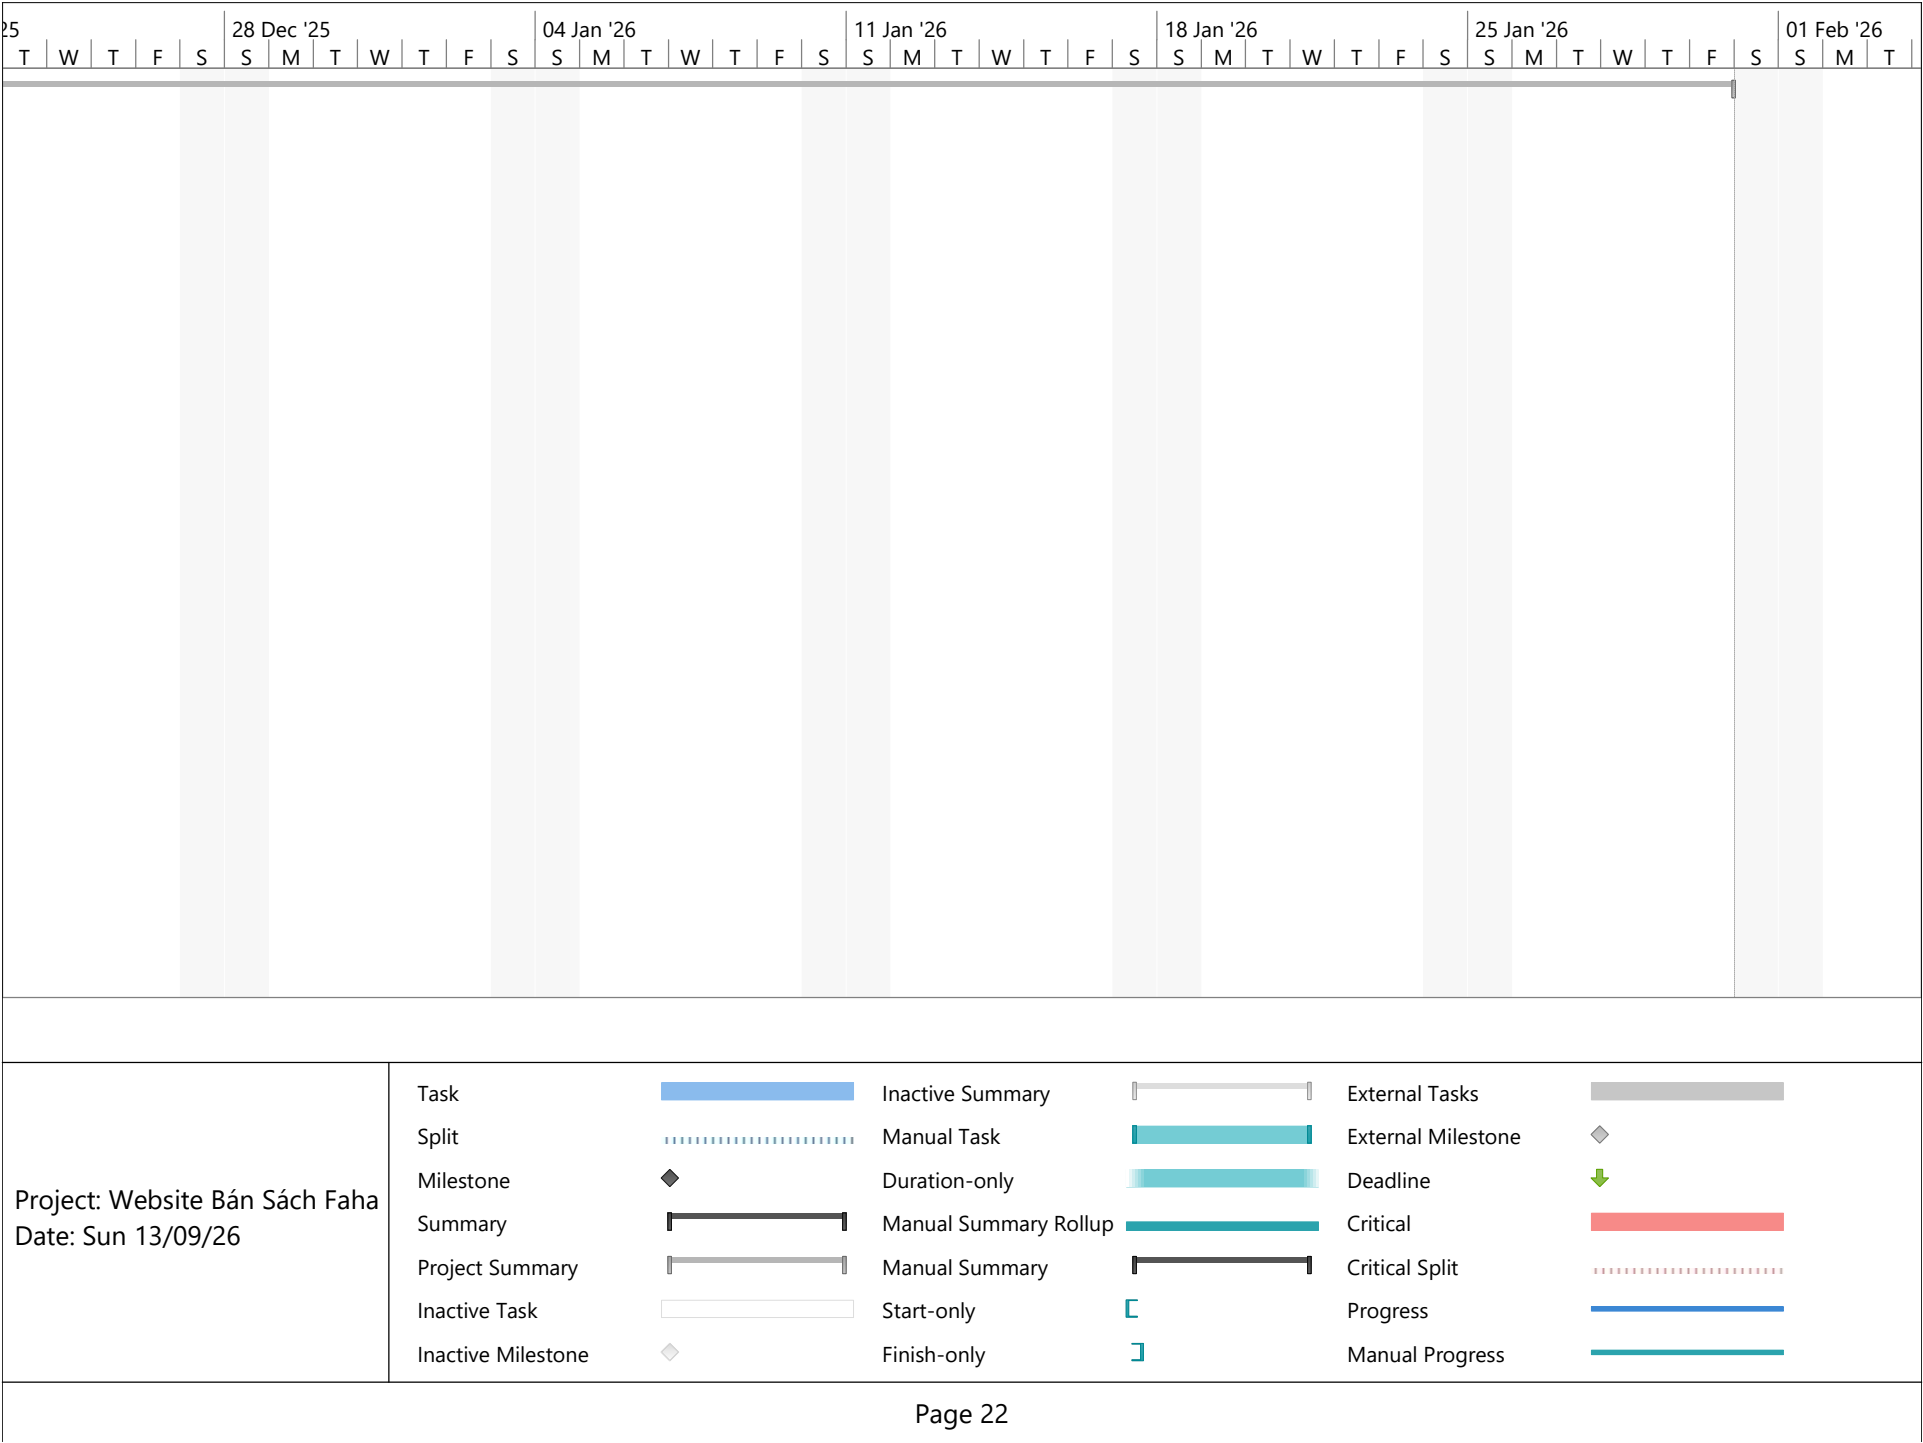




Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	




Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	




Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

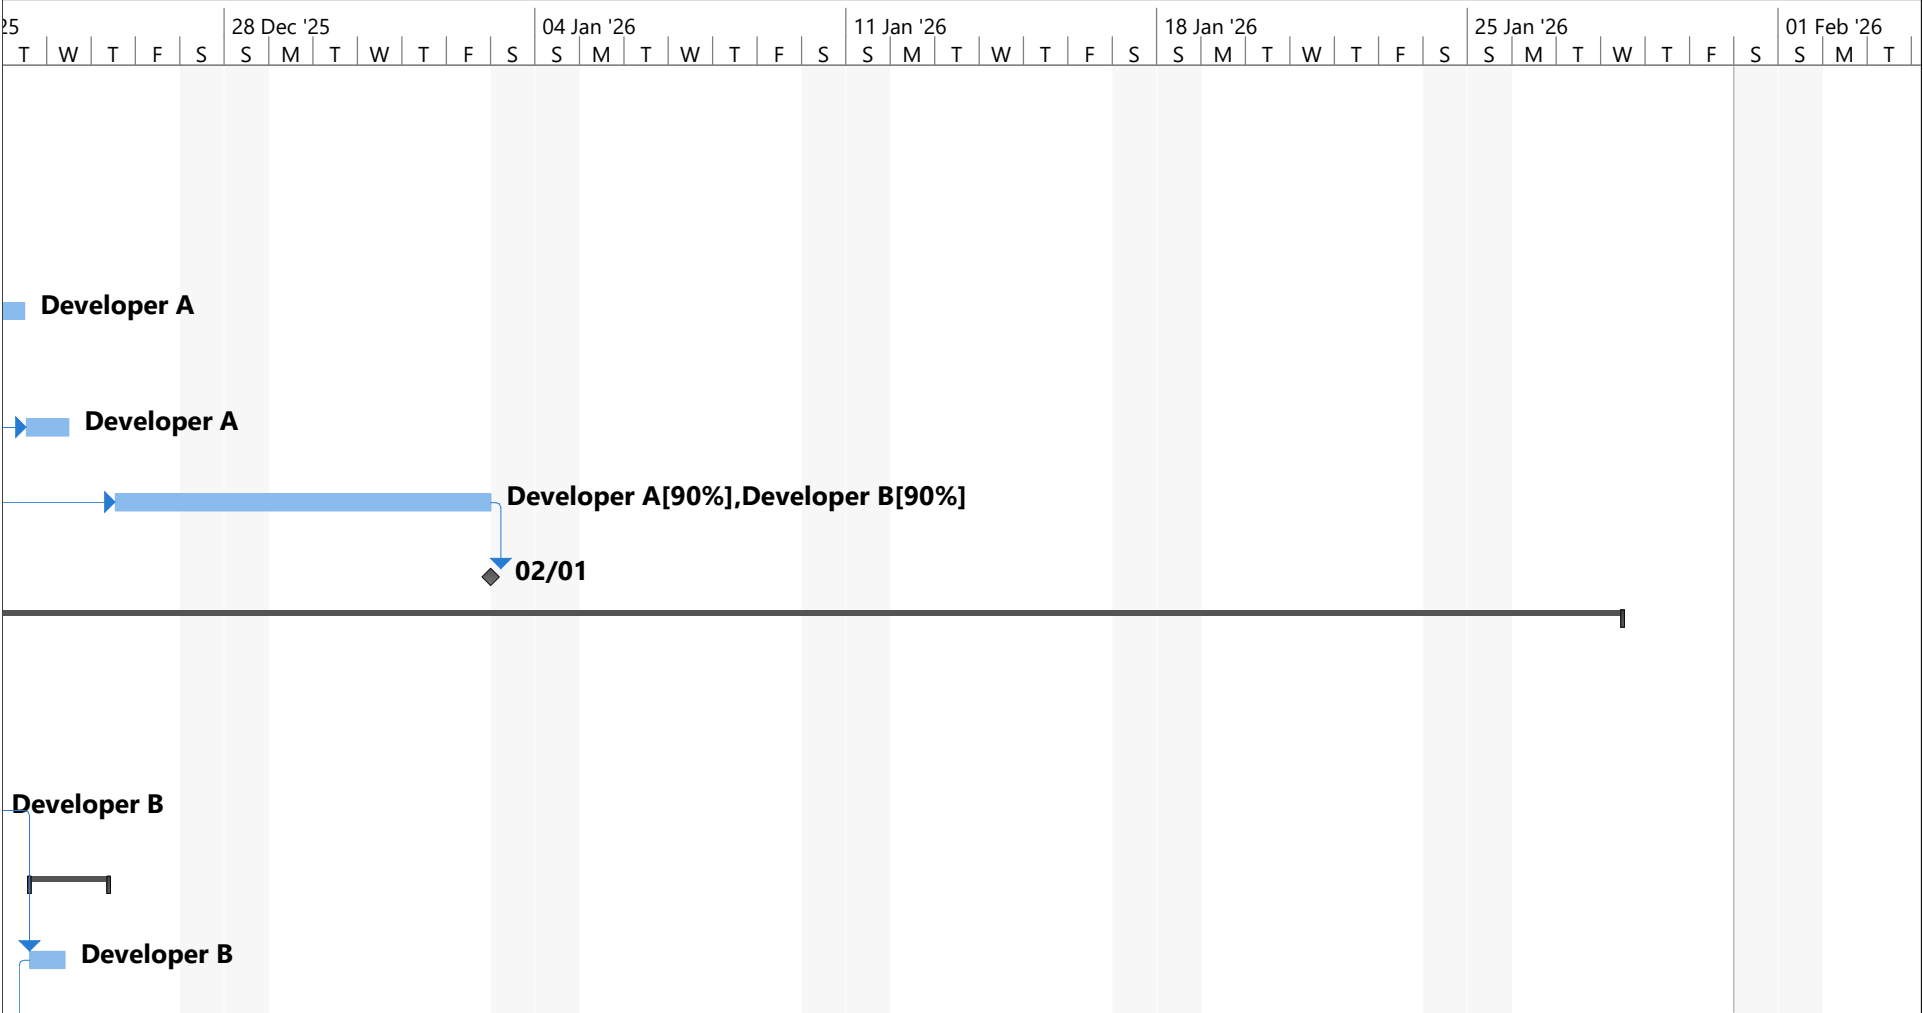

Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

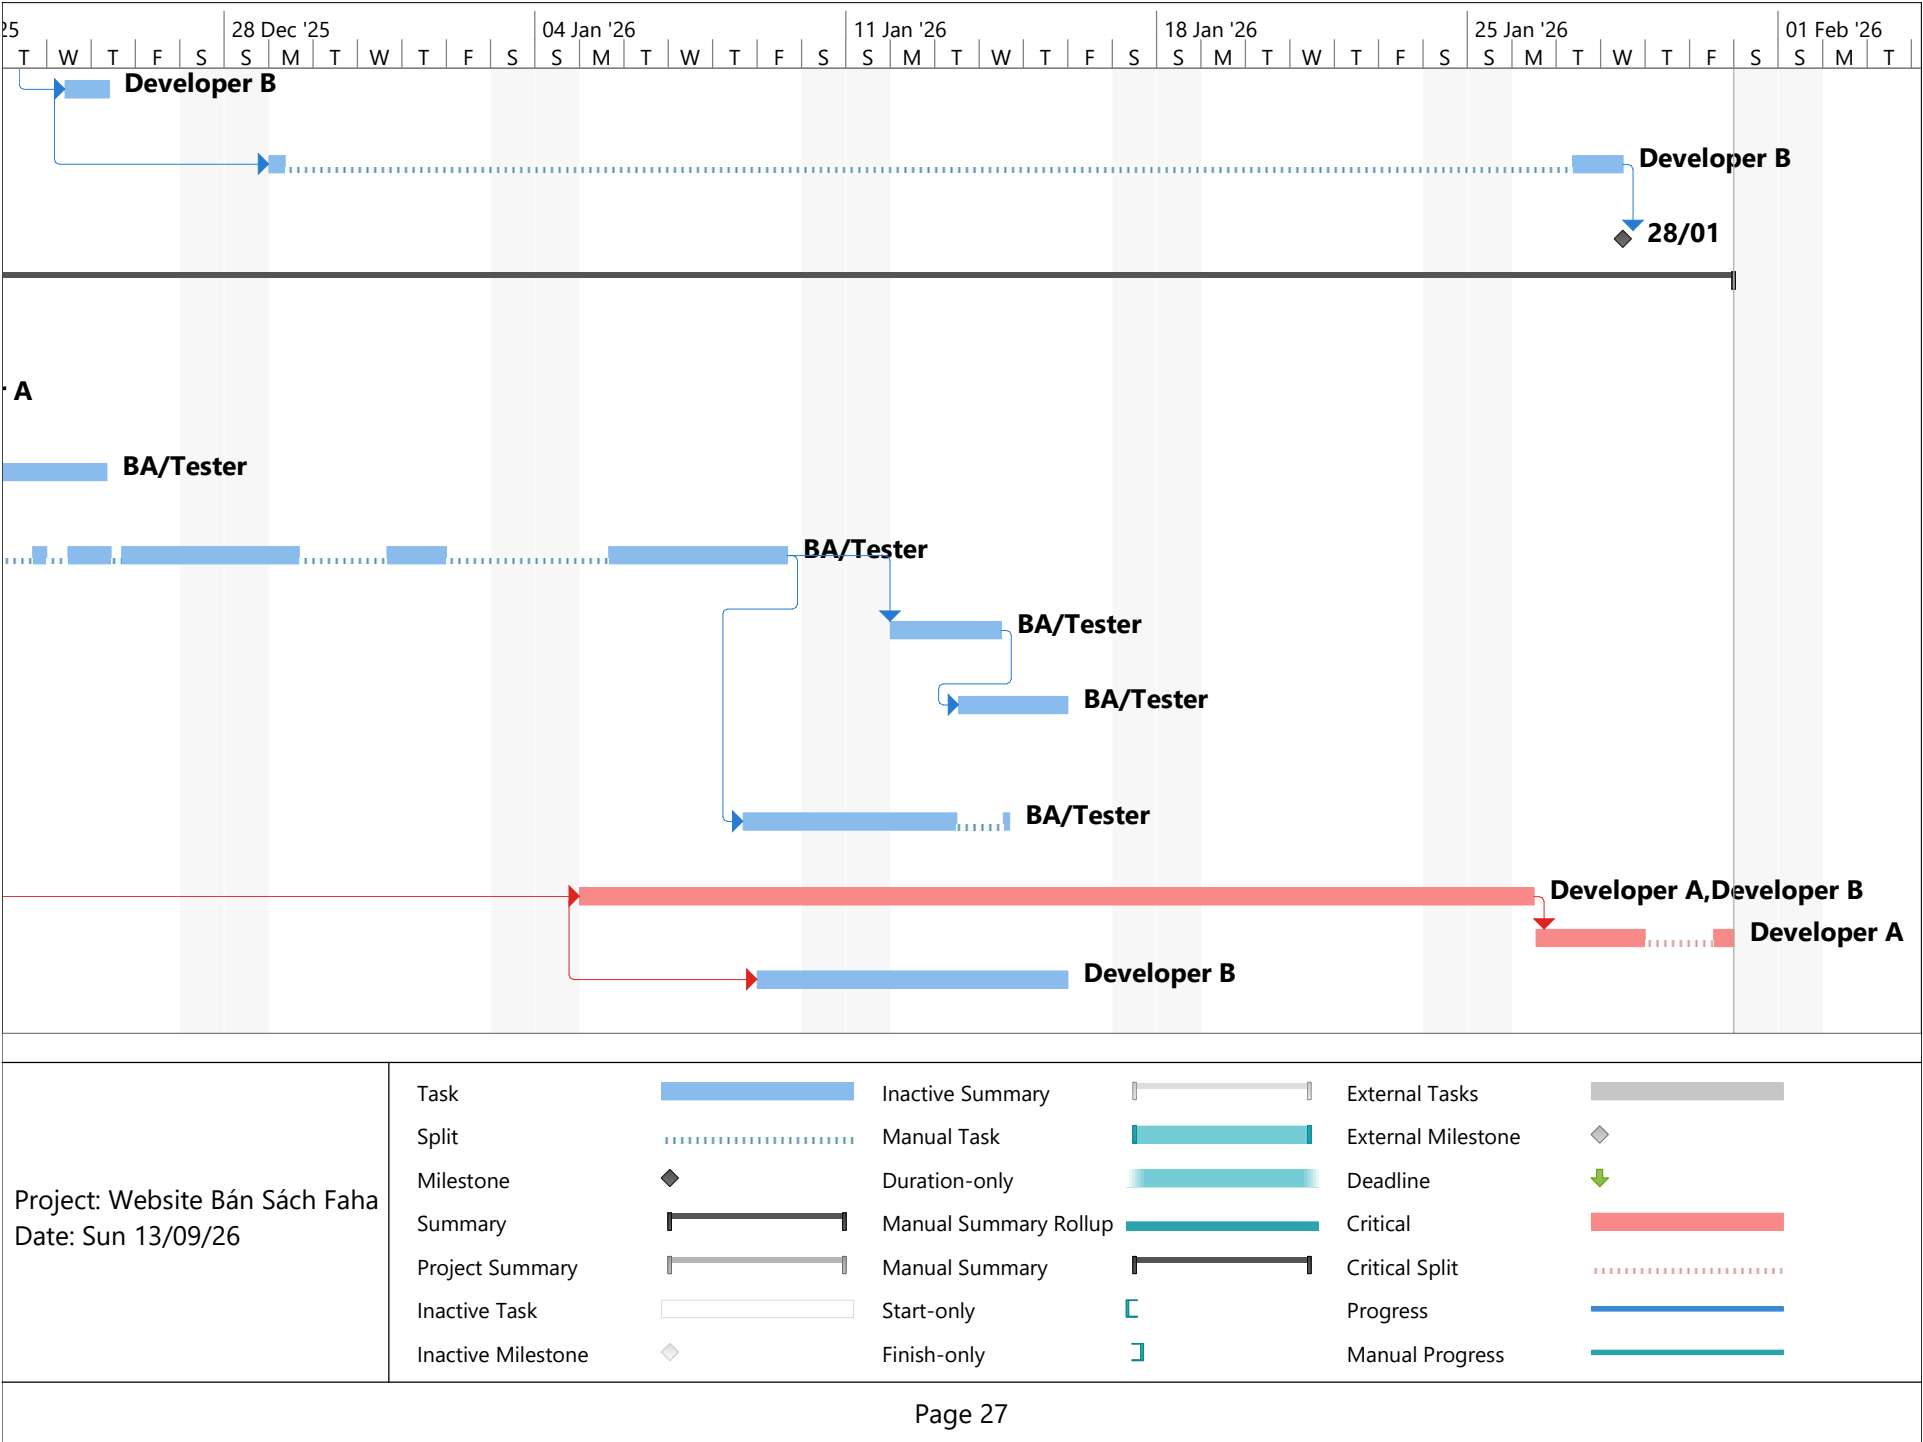



Project: Website Bán Sách Faha Date: Sun 13/09/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	
